

TILE RE-ROOF

1545 Northwest 15th Street Road, Miami, FL

DATE
Thu, Jul 9, 2026

JOB #
RWJ-0033

PREPARED BY
Chris Davis

WEATHER

6:00 AM

80°

Sunny

Wind 5 mph · Rain 0.00" · Hum 78%

12:00 PM

87°

Sunny

Wind 7 mph · Rain 0.00" · Hum 71%

4:00 PM

88°

Cloudy

Wind 9 mph · Rain 0.00" · Hum 77%





WORK LOGS

NAME	DESCRIPTION	HOURS
Chris Davis	8 roofers	—

GENERAL NOTES

- Crew tore off entire building and applied polyglass underlayment.
Found 4 rotted plywoods that where replaced.
Crew picked up at the end of the day using magnets

PHOTOS

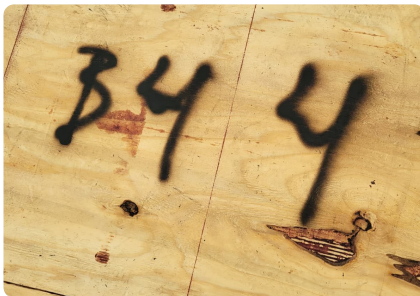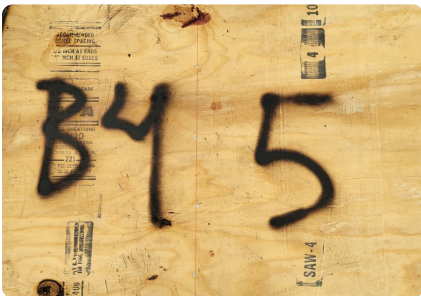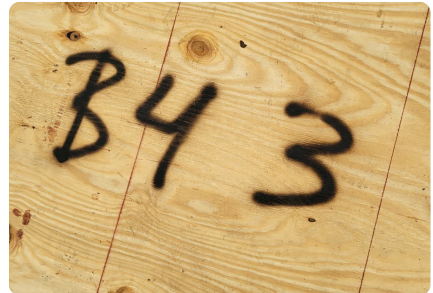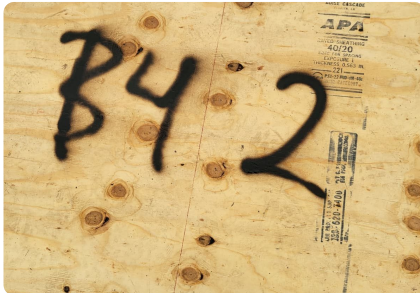

SITE SAFETY OBSERVATIONS

- 1. Safety cones and caution tape was placed around building.

QUALITY CONTROL OBSERVATIONS

- 1. Re-nailed deck according to code. apply bull around all penetrations.

SURVEY

1. Any accidents on site today?	NO	
2. Any scheduled delays occur?	NO	
3. Did weather cause any delays?	NO	
4. Any visitors on site?	NO	
5. Any areas that can't be worked on?	NO	
6. Any equipment rented on site?	YES	1 portable bathroom, 1 dumpster & 1 forklift

REVIEWED & APPROVED

Chris Davis
Jul 9, 2026, 11:57 PM
